

TRVA Briefing

Oct 18, 2011

Chickamauga Lock Replacement

Wayne Huddleston

Project Manager

Nashville District



US Army Corps of Engineers
BUILDING STRONG



Chickamauga Lock


Construction Contracts



BUILDING STRONG®

Chickamauga Lock

Design / Construction Schedule

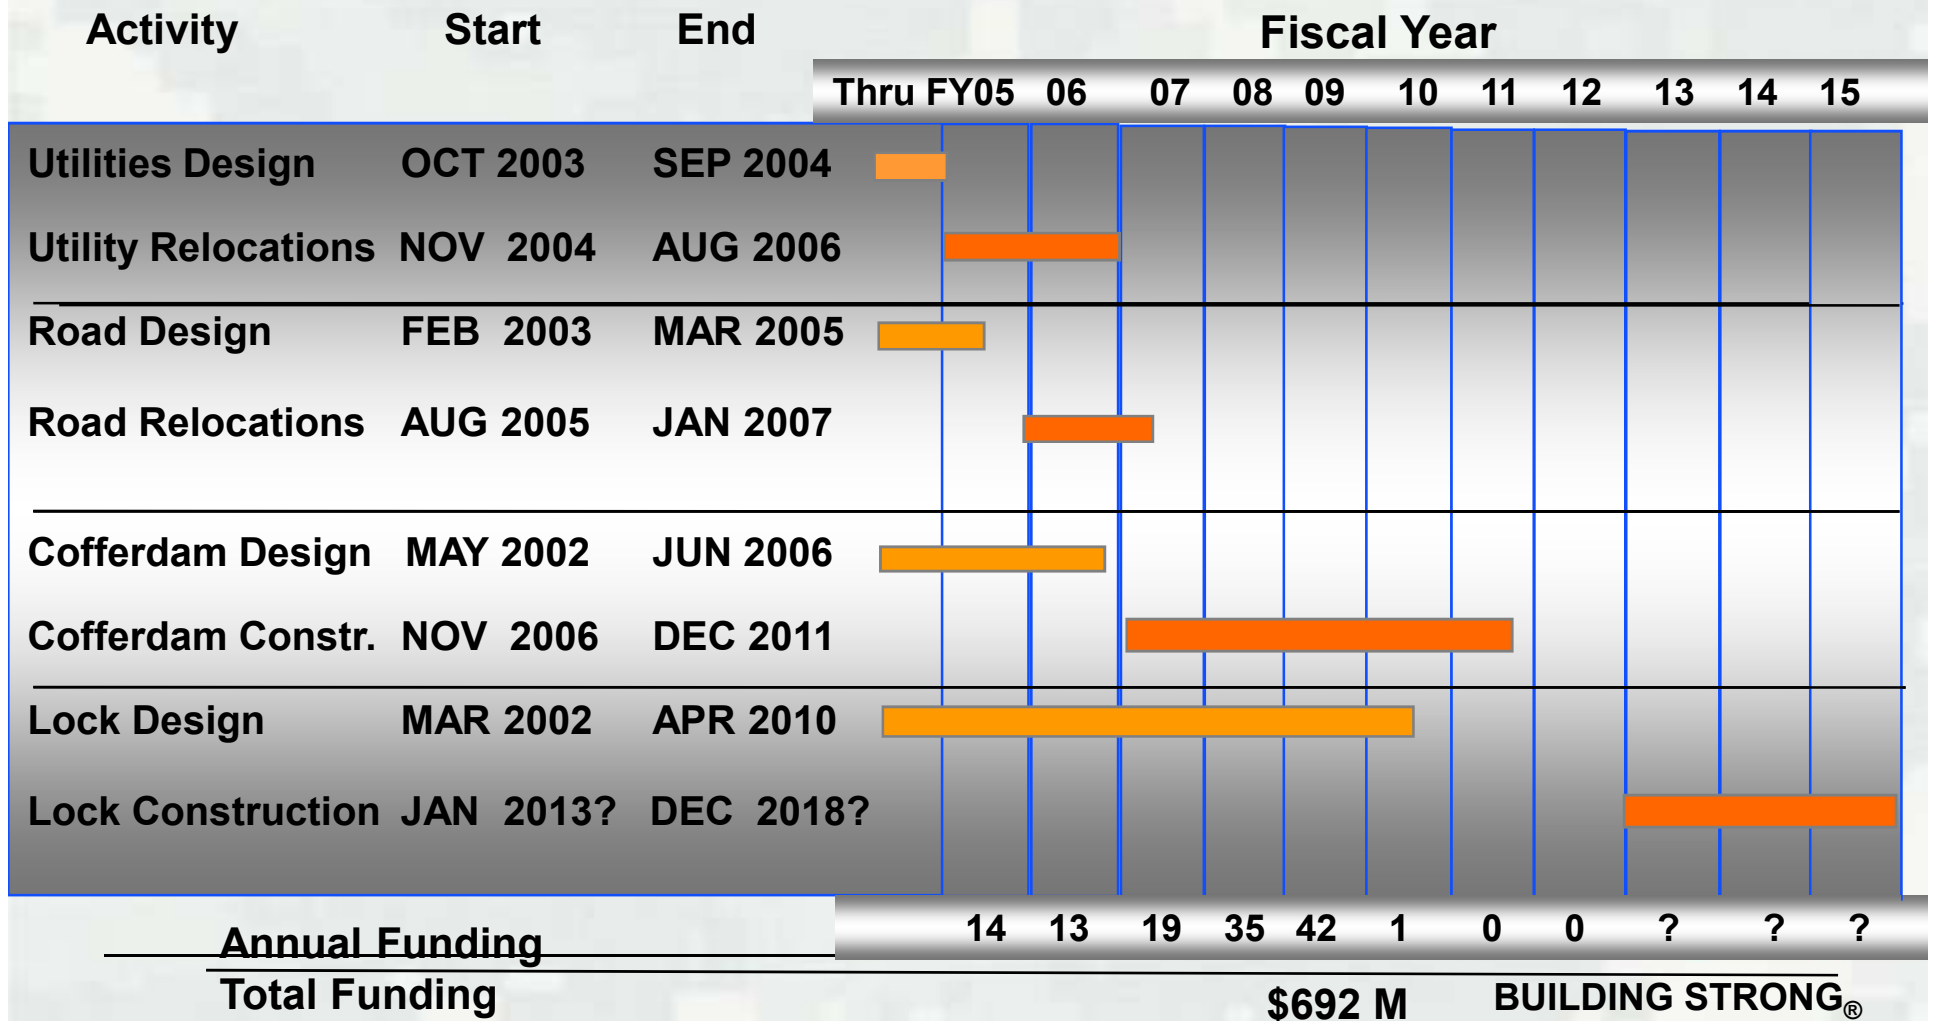

Chickamauga Lock

Road / Bridge Relocation



BUILDING STRONG®

Chickamauga Lock

Cofferdam Contract



BUILDING STRONG®

Chickamauga Lock

Cofferdam Contract – 99%



BUILDING STRONG®

Chickamauga Lock

Dewatering the Cofferddam



BUILDING STRONG®

Chickamauga Lock

Project Status

- **FY12**
 - Cofferdam Contract complete – Dec 11
 - Plan to halt all on-site construction – orderly closure
 - ARRA fabrications continue offsite – Sep 12
 - ARRA - Guide walls (\$14.1M) – Watts Bar
 - Miter gates, valves, bulkheads (\$17.0M) – Muscle Shoals
 - Aggressive Maintenance (\$3.1M)
 - Completed ds Gate Anchorage, horizontal bar installation
 - Finite Element Analysis, Replace ds quoin blocks



Chickamauga Lock

Gates, Valves, Bulkheads – ARRA



BUILDING STRONG®

Chickamauga Lock

Funding

Chickamauga Lock

- ▶ Existing ARRA funding will complete the cofferdam contract and off-site fabrication of lock gates, valves and approach walls in 2012. Lock funding is not anticipated until IWTF issues are resolved.
- ▶ Aggressive maintenance work (\$3.1M) for FY12. Additional Aggressive maintenance funding will be limited.



Chickamauga Lock

Lock Contract ??



BUILDING STRONG®
